Winnipeg Water Treatment Plant Project -- Bid Opportunity 171-2006

Revision 1
Date: Jan 3rd, 2007
Addendum 4

Schedule SCH # 1 for Precast Roof Panel Erection and Roofing installation (No topping).
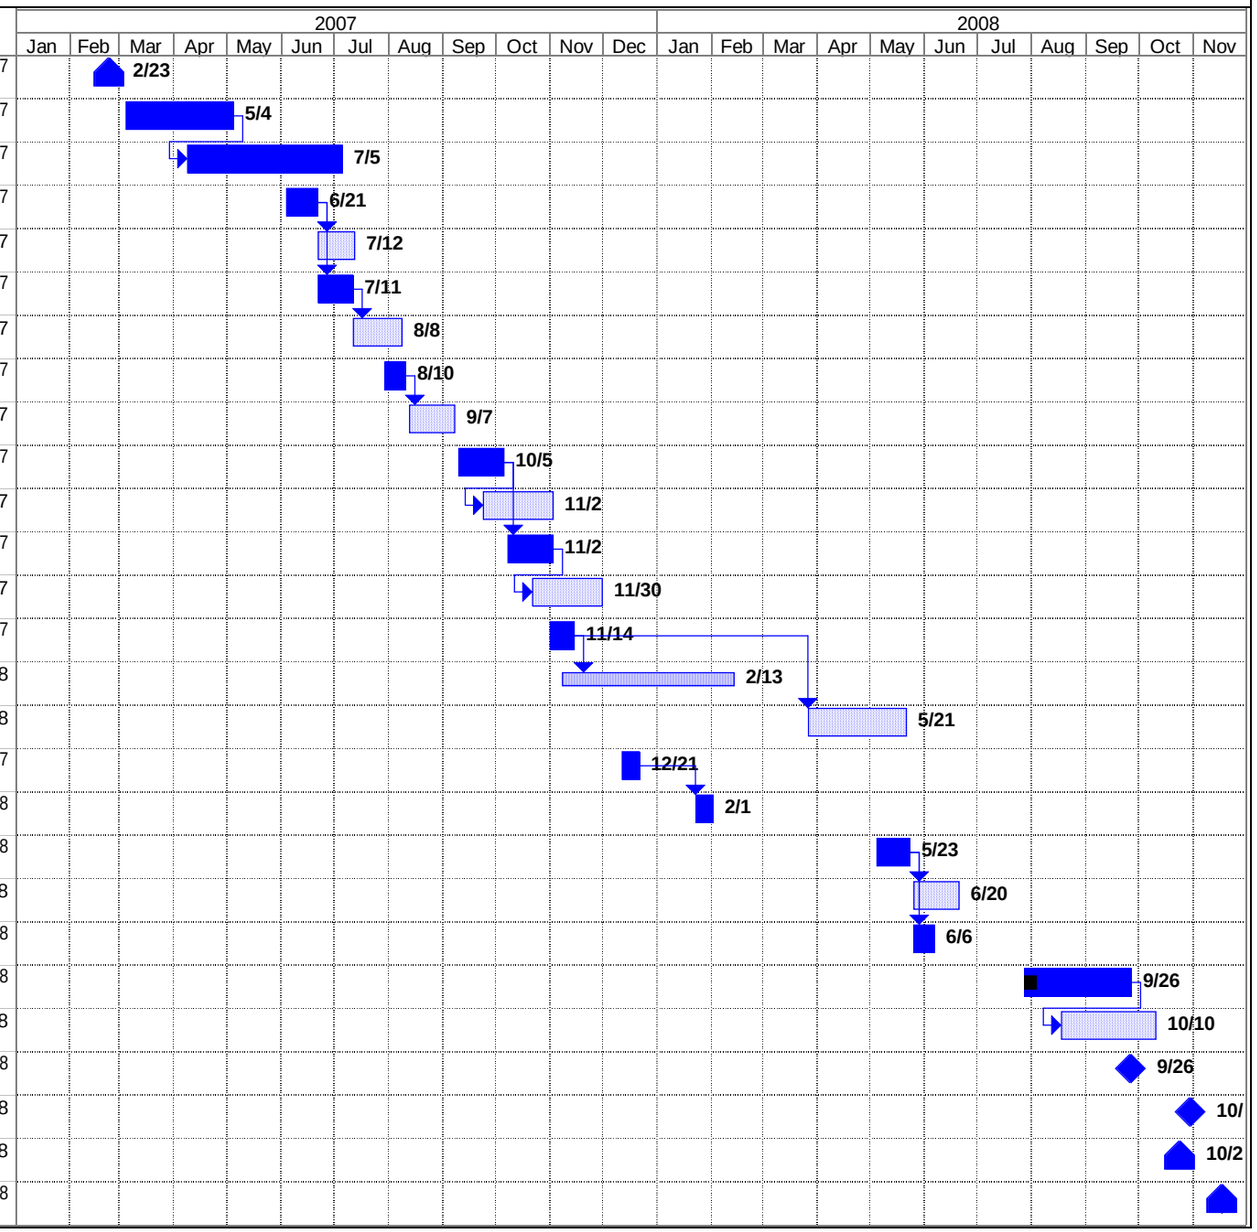
ID	Task Name	Duration	Start	Finish
1	Award Precast Roof Panels Contract	1 day	Fri 2/23/07	Fri 2/23/07
2	Shop Drawing Review period	45 days	Mon 3/5/07	Fri 5/4/07
4	Manufacture Precast panels	64 days	Mon 4/9/07	Thu 7/5/07
5	Erect panels to WI area	14 days	Mon 6/4/07	Thu 6/21/07
6	Install VB, insulation and roofing work (WI)	15 days	Fri 6/22/07	Thu 7/12/07
7	Erect panels to WM area	14 days	Fri 6/22/07	Wed 7/11/07
8	Install VB, insulation and roofing work (WM)	20 days	Thu 7/12/07	Wed 8/8/07
9	Erect Panels to WA Area	10 days	Mon 7/30/07	Fri 8/10/07
10	Install VB, insulation and roofing work (WA)	20 days	Mon 8/13/07	Fri 9/7/07
11	Erect Panels to WO Area	20 days	Mon 9/10/07	Fri 10/5/07
12	Install VB, insulation and roofing work (WO)	30 days	Mon 9/24/07	Fri 11/2/07
13	Erect Panels to WR Area	20 days	Mon 10/8/07	Fri 11/2/07
14	Install VB, insulation and roofing work (WR)	30 days	Mon 10/22/07	Fri 11/30/07
15	Erect panels to WF area (Grids B1 to B8)	10 days	Thu 11/1/07	Wed 11/14/07
16	Temporarily seal roof joints to area WF	70 days	Thu 11/8/07	Wed 2/13/08
17	Install VB, insulation and roofing work (WF)	40 days	Thu 3/27/08	Wed 5/21/08
18	Erect panels to WF area (Grids B8 to B15)	8 days	Wed 12/12/07	Fri 12/21/07
20	Erect panels to WF area (Grids B15 to B18)	8 days	Wed 1/23/08	Fri 2/1/08
21	Erect Panels to WC area	15 days	Mon 5/5/08	Fri 5/23/08
22	Install VB, insulation and roofing work (WC)	20 days	Mon 5/26/08	Fri 6/20/08
23	Erect Hollow Core slabs to WP area	10 days	Mon 5/26/08	Fri 6/6/08
24	Erect panels to WP area (Grids B2 to B19)	45 days	Mon 7/28/08	Fri 9/26/08
25	Install VB, insulation and roofing work (WP)	40 days	Mon 8/18/08	Fri 10/10/08
26	Substantial Performance - precast roof panel contract	1 day	Fri 9/26/08	Fri 9/26/08
27	Substantial Performance - roofing work	1 day	Thu 10/30/08	Thu 10/30/08
28	Total Performance - precast roof panels	1 day	Fri 10/24/08	Fri 10/24/08
29	Total Performance - roofing work	1 day	Mon 11/17/08	Mon 11/17/08
