SEWER JUNCTION INFORMATION
FOR SEWER ID MA20004193

REFERENCE–METERS SOUTH OF MANHOLE MH20003854

DIST. FROM REF. MANHOLE	JUNCTION DIA.	CLOCK REF.	SERVICE TYPE	DESCRIPTION
0.8	100	10	CN	–
2.4	100	10	CXI	–

REFERENCE–METERS NORTH OF MANHOLE MH20003850

DIST. FROM REF. MANHOLE	JUNCTION DIA.	CLOCK REF.	SERVICE TYPE	DESCRIPTION
5.2	100	02	JN	CAPPED
22.6	100	02	CN	–
24.3	100	03	CN	–
44.2	100	02	CN	–
46.5	100	12	CN	–
58.2	100	03	CN	–
74.6	100	03	CN	–

ALL JUNCTION INFORMATION
BASED ON CCTV INSPECTION

BYRON BAY (E. LEG)

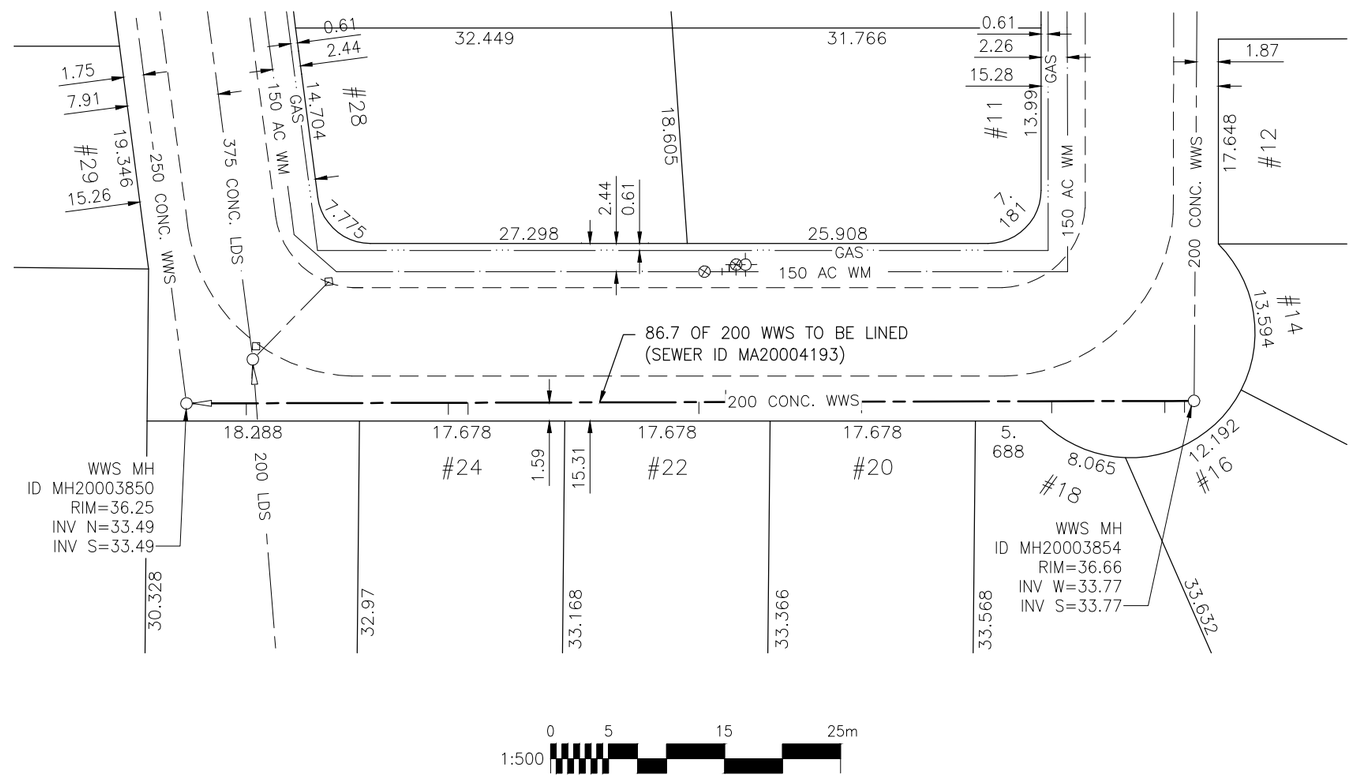

WARNING

IF POWER EQUIPMENT OR EXPLOSIVES ARE TO BE USED FOR EXCAVATION ON THIS PROJECT THE CONTRACTOR MUST:

1) NOTIFY THE GAS COMPANY OF THE PROPOSED LOCATION OF EXCAVATION.

2) TAKE PRECAUTION TO AVOID DAMAGE TO GAS COMPANY INSTALLATIONS.

SEE PROVINCIAL REGULATION 140/92 FOR DETAILS

METRIC

WHOLE NUMBERS INDICATE MILLIMETRES
DECIMALIZED NUMBERS INDICATE METRES

BENCH MARK: 83R494 – N.W. Cor. McBey Ave. & Kirkfield St., Tblt. on top of 0.05 m dia. x 2.4 m iron pipe, 5.4 m N. of C.L. Conc. Pav't. of McBey Ave. & 9.2 m W. of C.L. Conc. Pav't. of Kirkfield St., or 13.1 m N. of S.L McBey Ave. & on W.L. of Kirkfield St.

APEGM
Certificate of Authorization
Stantec Consulting Ltd.
No. 1301 Date:_____

BID OPPORTUNITY 927–2011

LOCATION APPROVED
UNDERGROUND STRUCTURES

SUPV. U/G STRUCTURES COMMITTEE — DATE

NOTE:
LOCATION OF UNDERGROUND STRUCTURES AS SHOWN ARE BASED ON THE BEST INFORMATION AVAILABLE BUT NO GUARANTEE IS GIVEN THAT ALL EXISTING UTILITIES ARE SHOWN OR THAT THE GIVEN LOCATIONS ARE EXACT. CONFIRMATION OF EXISTENCE AND EXACT LOCATION OF ALL SERVICES MUST BE OBTAINED FROM THE INDIVIDUAL UTILITIES BEFORE PROCEEDING WITH CONSTRUCTION.

B.M. 41–37
ELEV. 235.955m

NO.	REVISIONS	DATE	BY

Stantec Consulting Ltd.
905 Waverley Street, Winnipeg, Manitoba
Tel 204–489–5900 Fax 204–453–9012

DESIGNED BY	J.K.H.	CHECKED BY	W.A.B.
DRAWN BY	K.R.	APPROVED BY	H.A.K.
HOR. SCALE:	1:500	RELEASED FOR CONSTRUCTION:	
VERTICAL:	N/A		
DATE	2011.10.04	DATE	

ENGINEER'S SEAL

CONSULTANT DRAWING NO.
C-146

THE CITY OF WINNIPEG
WATER AND WASTE DEPARTMENT

2011 SEWER RENEWALS
BY CIPP LINING - CONTRACT 21
BYRON BAY (E. LEG)
MH AT BYRON BAY (N. LEG) (PL) TO
MH AT BYRON BAY (S. LEG) (PL)

SHEET 49 OF 119
CAD FILE DRAWING NUMBER 13220c-140-766.dwg
CITY DRAWING NUMBER 9815

\\CD1201-F02\work_group\1112\active\111213220\drawing\402_design\sheet_files\13220c-140-766.dwg
Date: 2011-12-19 2:01pm Login: Ammeter, Wes
