


STAGE 1 - PROPOSED WORKS

- ① INSTALLATION OF TEMPORARY CONSTRUCTION FENCING
- ② RELOCATION OF LIGHT STANDARDS
- ③ INSTALLATION OF LAND DRAINAGE SEWER
- ④ INSTALLATION OF SHORING AND EXCAVATION
- ⑤ APPROACH ROADWAY EXCAVATION
- ⑥ CONSTRUCTION OF GRAVITY WALLS
- ⑦ CONSTRUCTION OF CANTILEVER WALLS
- ⑧ CONSTRUCTION OF TUNNEL, BACKFILLING AND SLOPE GRADING
- ⑨ RECONSTRUCT QUINTEX & PEMBINA DODGE PARKING LOTS WITHIN PROJECT LIMITS
- ⑩ RELOCATION OF BELL FIBER OPTIC CABLE TO WEST SIDE OF C.N. PROPERTY (BY OTHERS)
- ⑪ RELOCATION OF ROGERS CABLE OVER COMPLETED TUNNEL (BY OTHERS)
- ⑫ CONSTRUCTION OF STAGE 2 TRACK DETOUR OVER COMPLETED STAGE 1 TUNNEL (BY OTHERS)
- ⑬ REMOVAL OF STAGE 1 TRACK DETOUR (BY OTHERS)

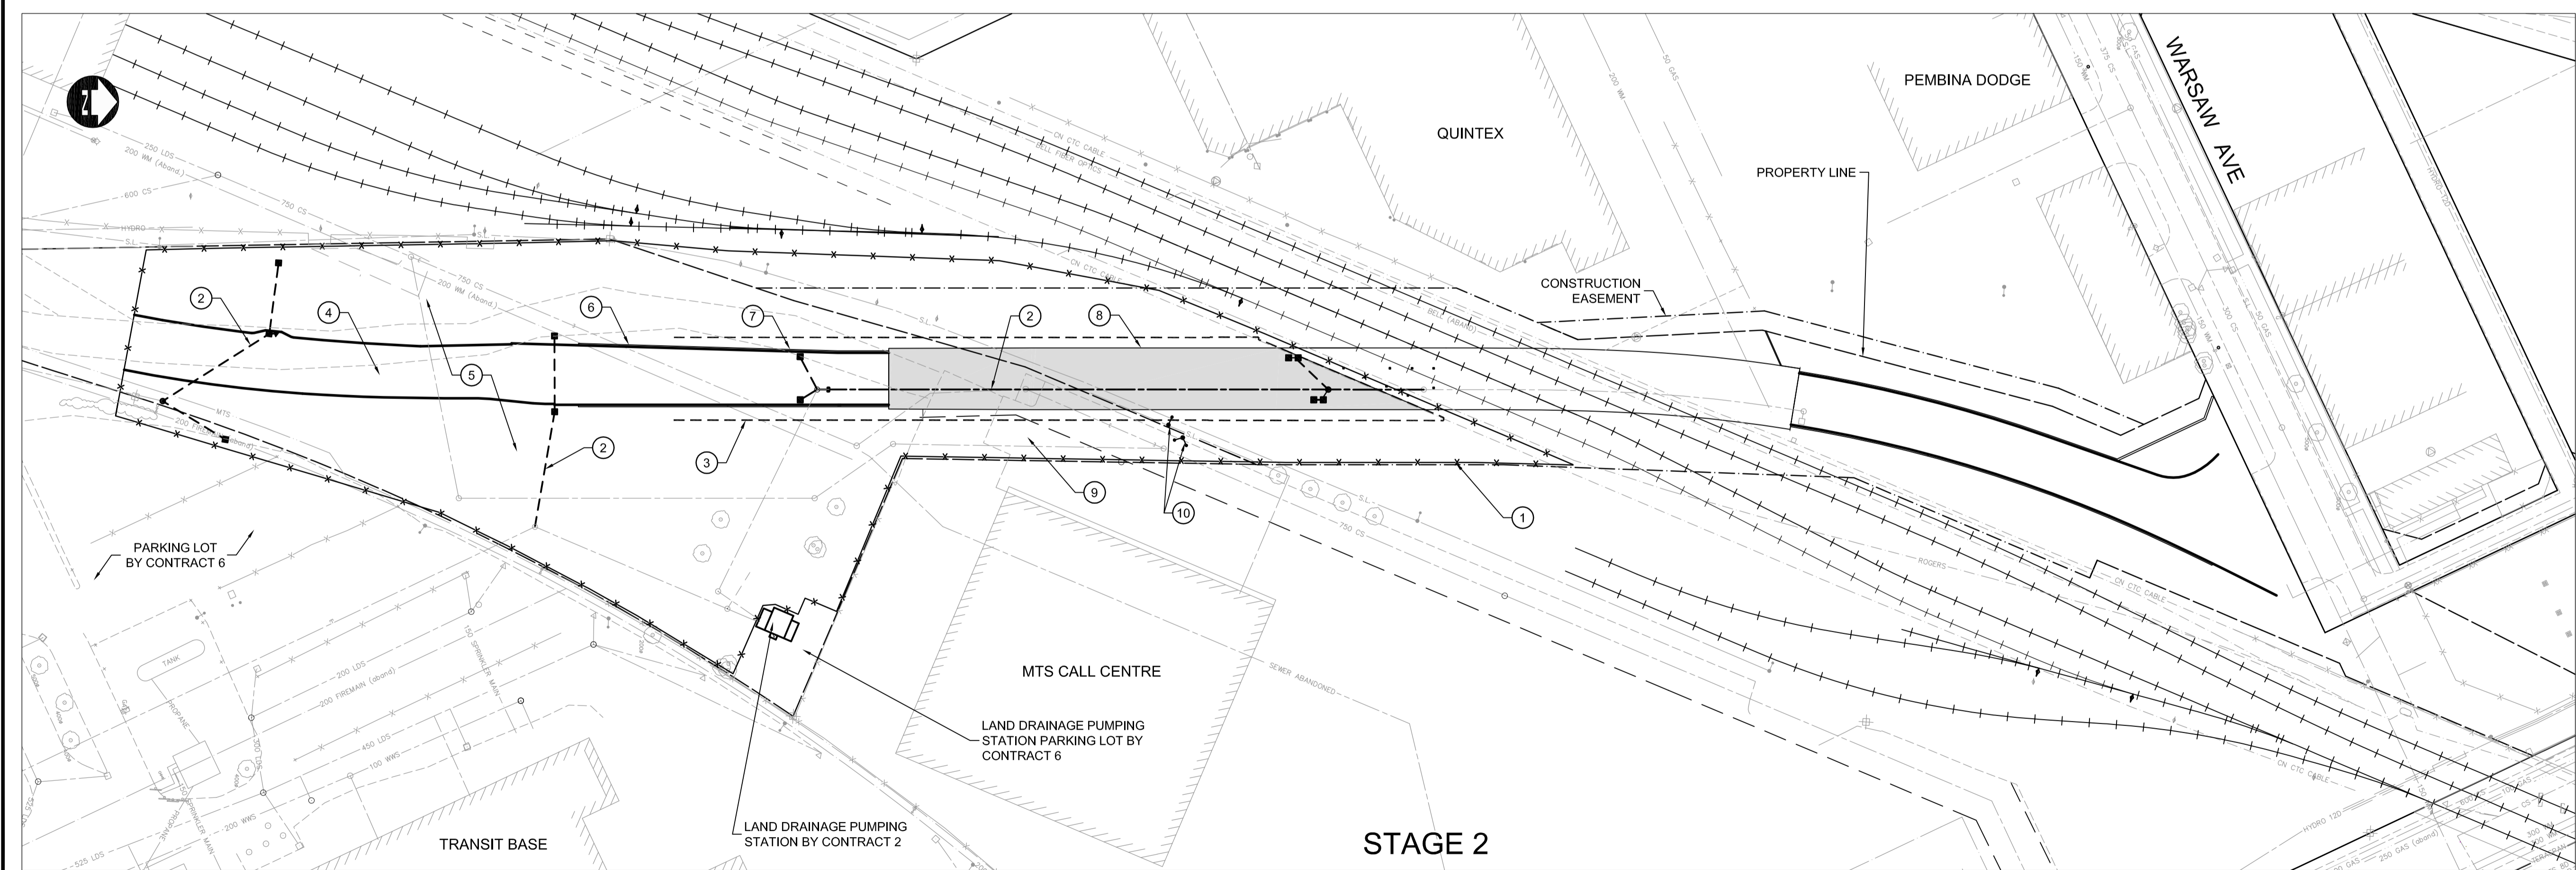

STAGE 2 - PROPOSED WORKS

- ① INSTALLATION OF TEMPORARY CONSTRUCTION FENCING
- ② INSTALLATION OF LAND DRAINAGE SEWER AND DRAINAGE INLETS
- ③ INSTALLATION OF SHORING AND EXCAVATION
- ④ APPROACH ROADWAY EXCAVATION
- ⑤ SITE GRADING
- ⑥ CONSTRUCTION OF GRAVITY WALLS
- ⑦ CONSTRUCTION OF CANTILEVER WALLS
- ⑧ CONSTRUCTION OF TUNNEL, BACKFILLING AND SLOPE GRADING
- ⑨ RECONSTRUCT MTS CALL CENTER PARKING LOT
- ⑩ REINSTALL VIA RAIL AND MTS LIGHT STANDARDS.



LOCATION UNDERGROUND	APPROVED STRUCTURES	B.M. ELEV.	DESIGNED BY	RTP
			DRAWN BY	TJH
			CHECKED BY	DPK
			APPROVED BY	DPK
			HOR. SCALE	1 : 750
			VERTICAL	
0	ISSUED FOR TENDER	10.13.2009	TJH	
NO.	REVISIONS	DATE	BY	DATE

0	ISSUED FOR TENDER	10.13.2009	TJH	
NO.	REVISIONS	DATE	BY	DATE

DILLON CONSULTING

ENGINEER'S SEAL

CONSULTANT PROJECT NO. 088813

THE CITY OF WINNIPEG
TRANSIT DEPARTMENT

Winnipeg

SOUTHWEST RAPID TRANSIT CORRIDOR - STAGE 1
TRANSITWAY TUNNEL AT CN RIVERS SUBDIVISION
MILEAGE 1.38 & ASSOCIATED WORKS

OVERALL STAGING PLAN AND MAJOR ITEMS
OF WORK

CITY DRAWING NUMBER: U237-09-04A
SHEET: 04A OF 73
CONSULTANT DRAWING NUMBER: C4-G103A-T
